


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0701
TRUNK HIGHWAY 14
COUNTY Blue Earth
DISTRICT 1A

LIMITS: In Mankato
N.W. End of Bridge (Minn River)-South Jct. T.H. 60



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Brick Pavement Br N ^o 411	74'		No Record of Constr. On Concrete Base 450 Conc. Arch.
1938	A.F.E. 43	Mixed Bitum.	32'	4"	Maint. Dept.
M	1948	Bit. Seal Coat	32'		AE-1, 387 Gal. Agg. 15 C.Y.
C	1948	Concrete	76'	5"	On old 6' Conc. base
C	1950	Plant Mix Bit.	74'	1 1/2" added	
C	1954	Foundation Protec- tion for Br. 411			
M	1972	Bit. Surface Overlay	76'	2 1/2"	MC-250-100 Gal. Agg. 220 Tons
C	1974	Bridge Repair Bit Surf. Overlay	31'	2 1/2"	

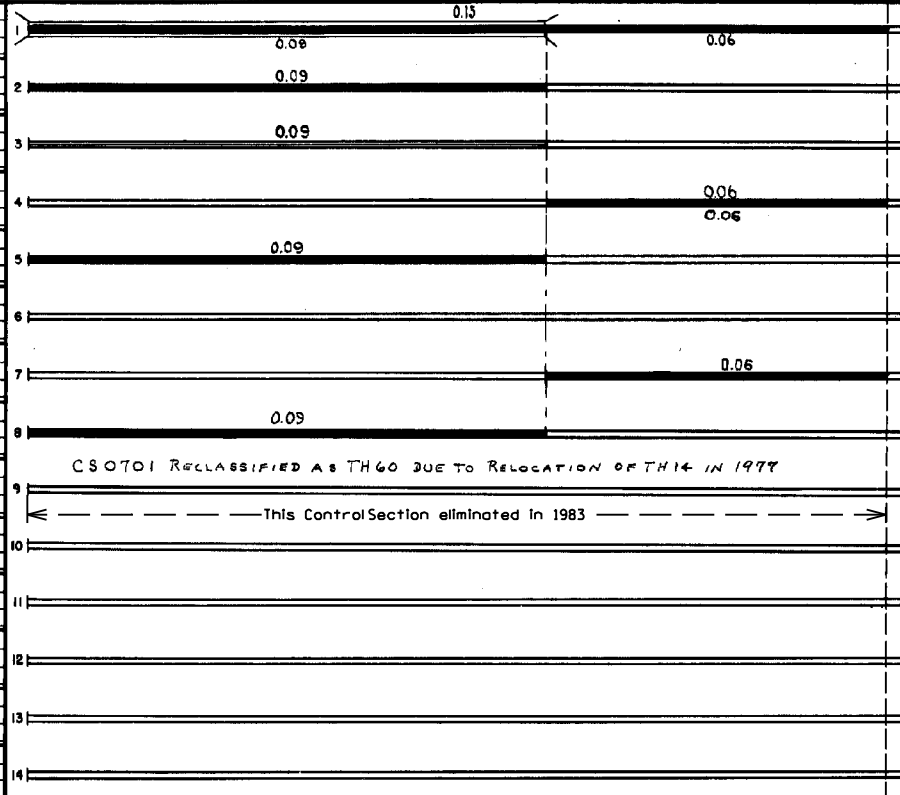

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921		0.15	0.00	0.00	0.06	0.09	0.00	0.00	0.06	0.09

REMARKS: Layout is to scale as of 1921
(1) Contract not final but work substantially complete in 1948.

A-74
