

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 8713  
TRUNK HIGHWAY 212  
COUNTY Yellow Medicine  
DISTRICT 8B

LIMITS: Jct. T.H. 59 - E. End of Bridge (Minn. River)

Ref. Pt. 035+00.116 - 035+00.339

YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	1"	No Record of Constr.
1927	212-12-30A	Grading Br. 4548	30'	27"	335 H.T. & L.T.
1928	212-12-30A	Gravel	26'	2"	
	(1)				
1929	212-12-30A	Oil Tr. Gravel	24'	1"	15809 Gal./Mile Maint. Dept.
1932	212-12-30B	Concrete	20'	9-7-9	
C		Replace Portals & raise lower cross frame on Br. 4548			By Bridge crew No. 2
C	1967 8713-01	Plant Mix Bit Gravel Shoulders	20'	4"	over P.C. Conc. inp.
C	1984 8713-05	Grading, Base Bit. Surface Bit. Shldr.	40' 36'	10" 2 1/4"	Sp. 2331 Sp. 2331, 2361
C	1984 8713-06	Approaches B Br. 87021			Repl. Br. 4548 322'
C	2004 1212-29	Bit. Overlay	24'	1.5"	Spec 2360
		Milling	28'	4"	
2012	8713-09	Conc. Paving Bit. Shldr	27' 8.5'	8" 3"	

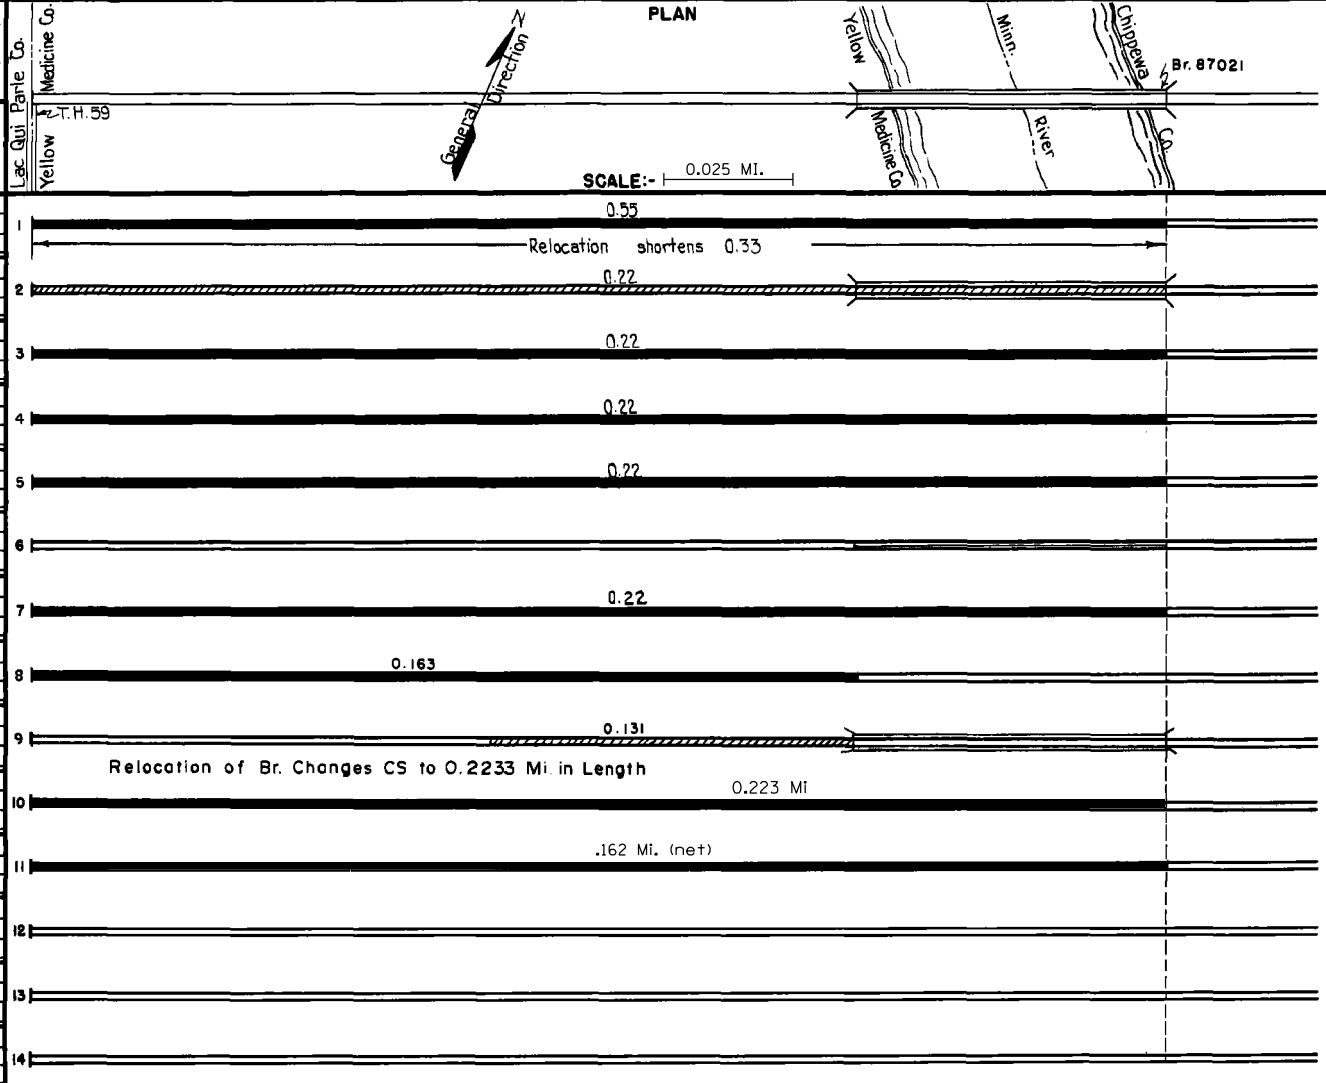

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1921 1926	0.55	0.00	0.00	0.00	0.00	0.55	0.00	0.00	0.00
1927	0.22	0.16	0.06	0.00	0.00	0.16	0.06	0.00	0.00

REMARKS: Layout is to scale as of 1927.  
(1) This work not done under this project number but lies within the limits of this project.
