

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 0403
TRUNK HIGHWAY
COUNTY Beltrami
DISTRICT 2A

LIMITS: West Co. Line - South Jct. T.H. 89

Ref. Pt. 110+00.059 + 116+00.960

Red Lake Indian Reservation PLAN

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o DIST
		TYPE	WIDTH	THICKNESS	
		Earth			No Record of Constr. Added in 1934.
1936		Gravel	26'	2"	Maint Dept.
C		Grading	36'		
1956	0403-02	Select Gran. Matl. Gravel Surface	36'	12" 1 1/2"	155
C		Bit. Surfacing	24'	1 1/2"	MC-1&2, 115714 Gal. Agg. 72.86 Tons
1957	A.F.E. 822	Mixed Bit. (Mixed Prime)	24'	1 1/2"	1357
M		Light Bit. Seal	25'		RC-2, 12525 Gal. Agg. 424 C.Y.
1959	A.F.E. 605	Light Bit. Seal	25'		1459
M		Light Bit. Seal	25'		RS-1C, 11571 Gal. Agg. 440 C.Y.
1965	C	Light Bit. Seal	25'		465
M		Bit. Resurface	24'	1 1/2"	
1972	SF	Bit. Resurface	24'	1 1/2"	1972
C		3-CABLE GUARDRAIL			1200 LIN. FT.
1978	0403-03	3-CABLE GUARDRAIL			1200 LIN. FT.
M		Bit. Overlay	24'	1 1/2"	2,460 Ton
1983	SF	Bit. Overlay	24'	1 1/2"	2,460 Ton
		Gravel Shouldering	5'	2"	3,862 Ton
C		Bit. Overlay	24'	3"	Spec 2331
1986	0403-06	Bit. Overlay	24'	3"	Spec 2331
		Bit. Shouldering	4'		
S		Widening			
2007	0403-07	Bit. Overlay	var	2 1/2"	Spec. 2360
		Aggregate Shldr	2'	2 1/2"	Class 1

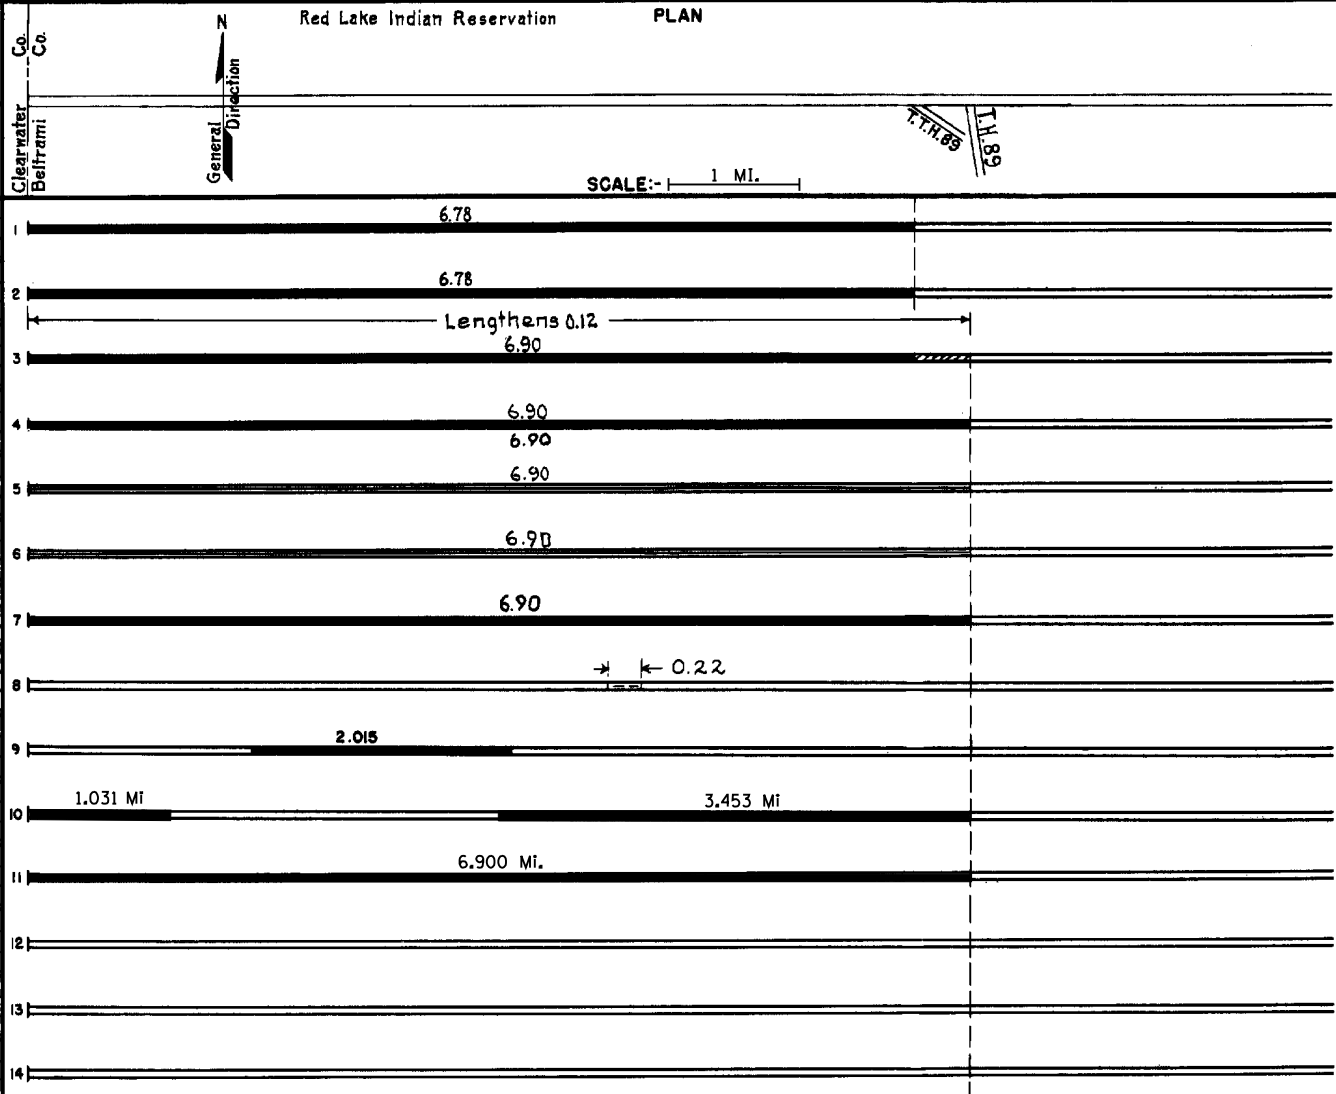

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1934	1955	6.78	6.78	0.00	0.00	0.00	0.00	6.78	0.00	0.00	0.00
1956		6.90	6.90	0.00	0.00	0.00	0.00	6.90	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1934
