


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0607
TRUNK HIGHWAY 75
COUNTY Big Stone
DISTRICT 4B

LIMITS: N. End Br. (Minn River) - Jct. T.H. 12 in Ortonville



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr.
1920	75-6-20-C,D&E	Gravel	20'	2"	
1927	75-6-20-C	Tar Tr. Gravel	20'	1 1/2"	10150 Gal/Mile. Maint. Dept.
1927	75-6-49	Mono. Culvert			W46 & W64.
1928	75-6-20-D&E	Tar Tr. Gravel	26'0"	1"	7877 Gal/Mile. Maint. Dept.
1929		Tar Tr. Gravel	VM	1"	Maint. Dept.
1932	75-6-55-1A	Gravel	30'	1 1/2"	900 C.Y./Mile. Br. 5174 & 6251
1933	75-6-55-1A	Gravel	30'	3/4"	2800 C.Y./Mile.
1935	75-6-55-1A	Asph. Tr. Gravel	30'	1"	15600 Gal/Mile. Maint. Dept.
1937	75-6-55-3A&B	Grading CaCl ₂ Stab. Grav.	32' 26'	2"	
1938	0607-01A&01B	Mixed Bitum.	24'	1"	
M	1940 A.F.E. 12	Bit. Seal Coat			Em. 1 Ass. 4009 Gal./Mi. Grav. 68 C.Y./Mi. Maint. Dept.
M	1942 A.F.E. 5	Bit. Seal Coat			AE-1 Em. 3367 Gal./Mi. Grav. 104 C.Y./Mi. Maint. Dept.
M	1944 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		Bit. 874 Gal./Mi. Grav. 30 C.Y./Mi. Maint. Div.

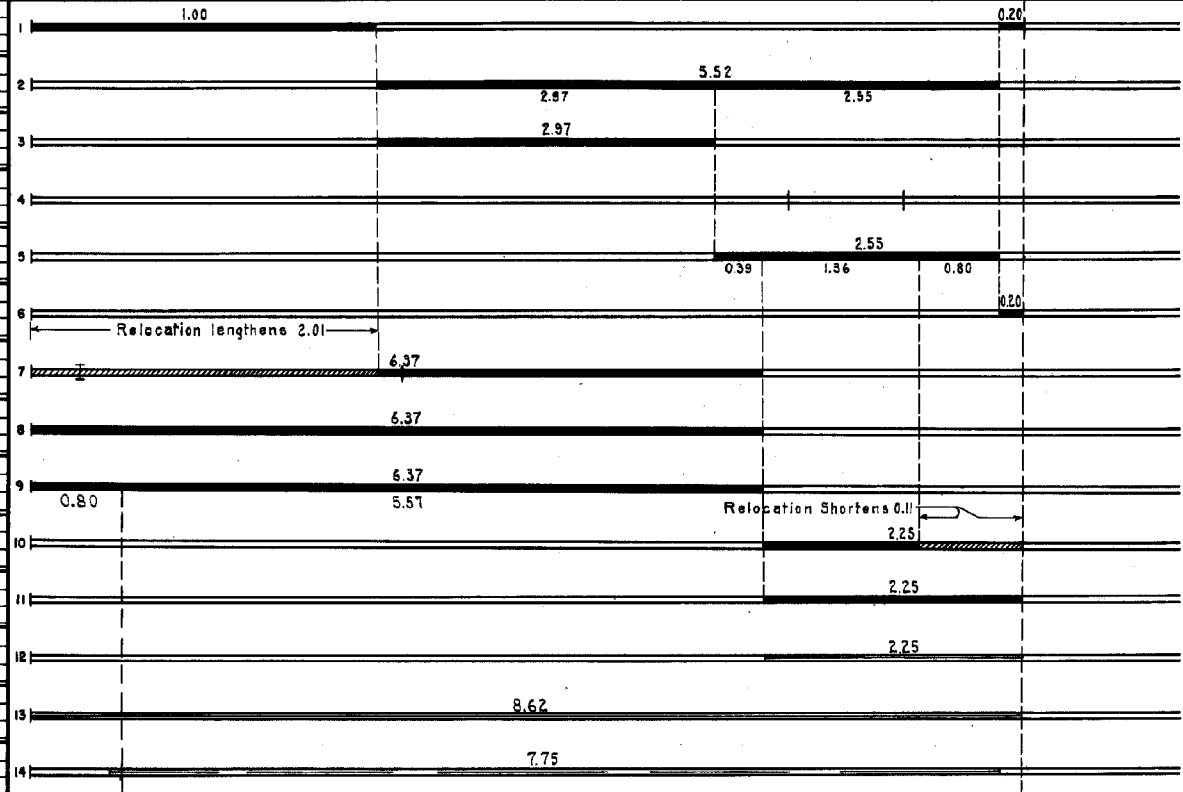

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN		REMARKS: Layout is to scale as of 1937
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1921	1931	6.72	4.47	0.00	2.25	0.00	5.72	0.00	1.00	0.00	
1932	1936	8.73	6.71	0.02	2.00	0.00	7.71	0.02	1.00	0.00	
1937	1953	8.62	7.71	0.02	0.89	0.00	7.71	0.02	0.89	0.00	
1954	1960	8.61	7.72	0.02	0.87	0.00	7.72	0.02	0.87	0.00	
1961	1967	8.61	7.99	0.02	0.60	0.00	7.99	0.02	0.60	0.00	
1962		8.61	7.72	0.02	0.87	0.00	7.72	0.02	0.87	0.00	

REMARKS: Layout is to scale as of 1937

(1) This work not done under these project numbers but lies within the limits of these projects

