


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0911
TRUNK HIGHWAY 61
COUNTY Carlton
DISTRICT 1A

LIMITS: Jct. T.H. 45 in Scanlon - E. Co. Line



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
1924	61-1-42	Grading Concrete Br. 4004 & 4005	32' 18' 19'	7 1/2"	
1936	61-1-42	Br. 4005	36'		480' H.T. & 76 B.S.
1938	0911-04	Pit Scale Station & Gravel Base Widening	20'	6"	10' Rt. & Lt.
1938	61-1-42	Concrete Widen.	20'	9-9"	10' Rt. & Lt.
1939	A.F.E. 12	Seeding			Maint. Dept.
1939	A.F.E. 43	Improve Shoulders			Maint. Dept.
C	0911-14	Grading Gravel Base	38' 38'	18"	New S.B. Roadway & Grade Widening
C	0911-14	Grading			Divided Highway
1949	0911-17	Bit. Stab. Grav. Base Mixed Bit.	27' 466'	12-18" 1"	
C	0911-19	Plant Mix Bit.	466'	3"	
(2)	0911-16	Widen Br. 4005	52'		70' B.S.
C	0911-11				
1954	0911-20	Br. 5984	28'		3-162' H.T.
	0911-23	Traffic Signals			
C	0911-21	Sand-Grav. Sub-base Bit. Stab. Base Plant Mix Bit.	37' 74' 48'	12 min 6-Var 3"	(Sub-base on N.B. Rdwy.)
M	1956	Spot Treat Bit. Surf. Repair & Bit. Seal	24'		5C4 & MG2, 2775 Gal. Agg. 162 Tons & 23 CY
M	1957	Spot Treat Bit. Surf. Repair			Plant Mix 185 Tons
M	1958	Spot Treat Bit. Surf. Repair	24'		Plant Mix 92 Tons (0.03 Mi. on Service Dr.)

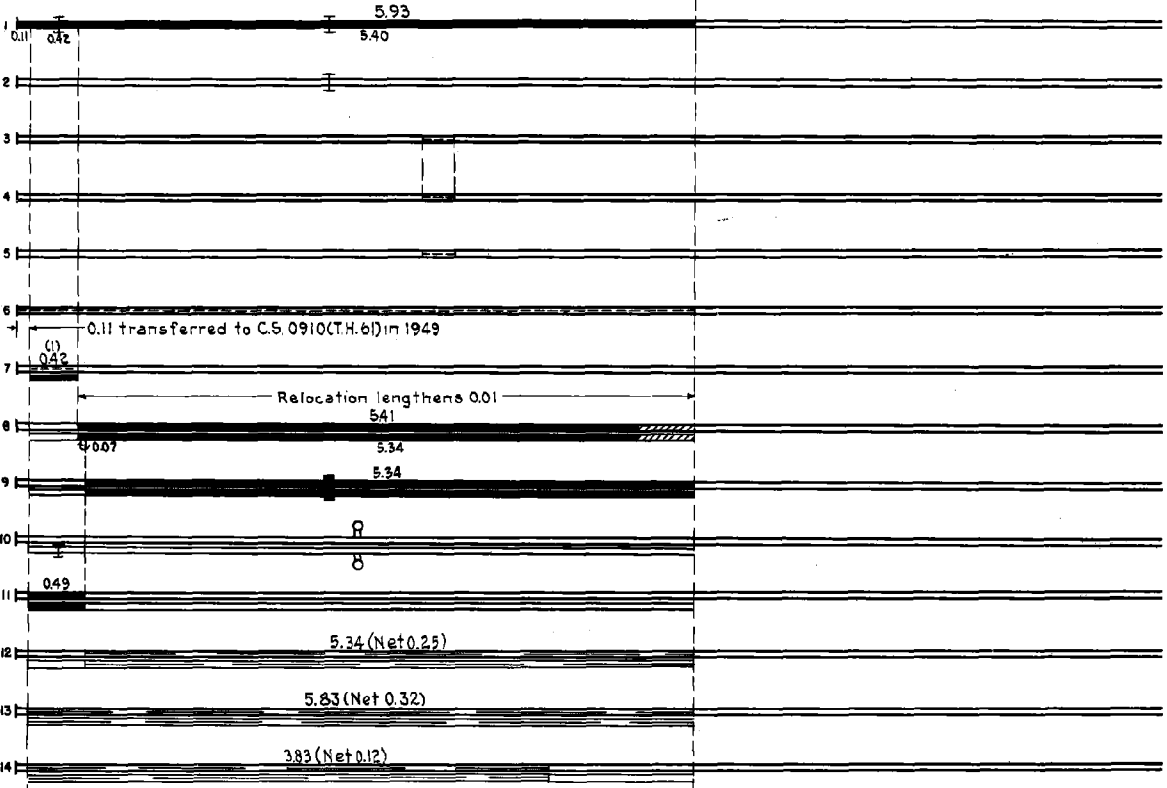

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.	ROWY. MI.	BR. MI.
1924	1948	5.93	5.50	0.11	0.32	0.00	5.82	0.11	0.00	0.00
1949	1973	5.83	5.51	0.11	0.21	0.00	5.72	0.11	0.00	0.00
1974	1975	0.77	0.47	0.09	0.21	0.00	0.68	0.09	0.00	0.00
1976										

REMARKS: Layout is to scale as of 1924
(1) .42 mi. of new S. bound roadway not in use until new St. Louis River bridge is built. (2) Contract not final on S.D. 0911-19 but work substantially complete in 1950.

6-76

