

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 1107
TRUNK HIGHWAY 200
COUNTY Cass
DISTRICT 3A

LIMITS: Jct. T.H. 84 - Jct. T.H. 6 near West Corp. Limits of Remer

Leech Lake Indian Reservation Chippewa National Forest PLAN

Remer
0.00 Mi.

YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
		Earth	26' 34"		No Record of Constr.
		Earth	24'		No Record of Constr.
		Earth	20'		No Record of Constr. Taken over in 1926.
1926	34-34-23-2	Grading Gravel	26' 20' 34"	2 1/2"	1200 C.Y./Mile.
1932	34-34-27	Grading Gravel Br. No 5217	32' 20' 27'	5"	1700 C.Y./Mile. 198 D.P.G.
1938	1937 A.F.E. 47 1938 A.F.E. 32	Mixed Bit. Surface	24'	1"	Maint. Dept.
M	1940 A.F.E. 8	Bit. Seal Coat			AE-1, 3614 Gal./Mi. Agg. 92 C.Y./Mi. Maint. Dept.
C	1942 1107-01	Grading Gravel	36'		954 C.Y./Mile.
C	1942 A.F.E. 7	Seeding			Seeds supplied by R.S.D. (S.P. 1107-04) Maint. Dept.
M	1943 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		RF-6, 737 Gal./Mi. Maint. Dept.
M	1945 1107-06	Base Repair (Spots) Bit. Prime Coat (Spots)	32' 32'	6-12"	3/4 Gal./50 Yd.
M	1945 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		MC-2, 2184 Gal./Mi. Grav. 200 C.Y./Mi. Maint. Div.
M	1945 A.F.E. 6	Grav. Resurfacing			334 C.Y./Mi. Maint. Div.
C	1946 A.F.E. 16	Bit. Resurfacing Mixed Bit.	24'	3/4-1 1/2"	SC-4, 94623 Gal. Agg. 4025 C.Y. Added

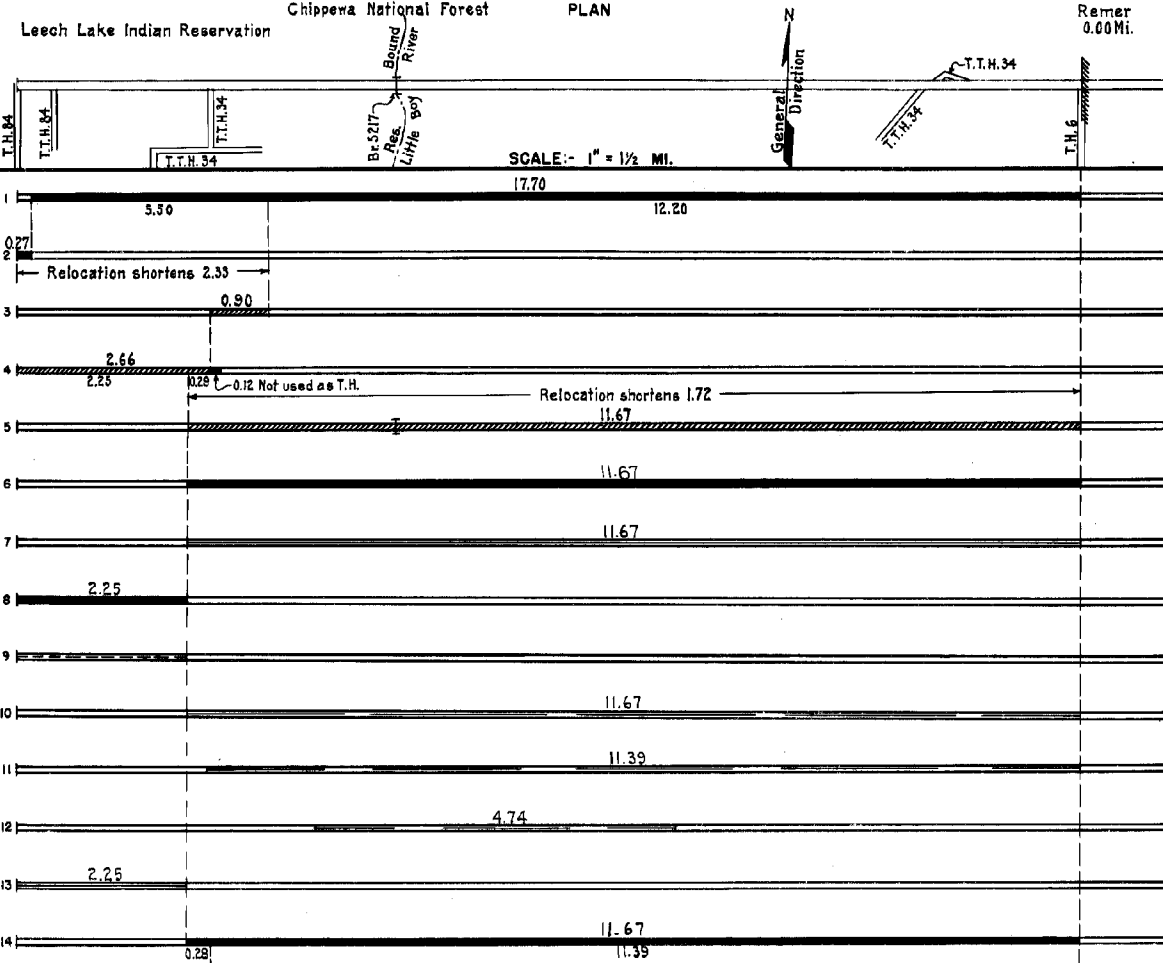

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1923	1925	17.97	17.97	0.00	0.00	0.00	17.97	0.00	0.00	0.00
1926	1931	15.64	15.64	0.00	0.00	0.00	15.64	0.00	0.00	0.00
1932	1962	13.92	13.88	0.04	0.00	0.00	13.88	0.04	0.00	0.00
1963	1970	13.90	13.86	0.04	0.00	0.00	13.86	0.04	0.00	0.00

REMARKS: Layout is to scale as of 1932

