

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1207
TRUNK HIGHWAY 29
COUNTY Chippewa
DISTRICT 8A

LIMITS: W. Jct. T.H. 40 - E. Jct. T.H. 40.

YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°	PLAN
		TYPE	WIDTH	THICKNESS		
1920	29-38-4	Grading Br. 8121 3315 & 8122	24' 24' 20 3/4'			
1921	29-38-4	Gravel	20'	3"	1200 C.Y./Mile.	
1931	29-38-4	Oil Tr. Gravel	20'	1"	10711 Gal./Mile. Maint. Dept.	
1940	1207-01	Br. 3315 Widen Br. 8121 Br. 8122 Removed	24'		18' C.S. (Culvert) W104. Replaced by C.M.	
1940	A.F.E. 21	Spot Treat. Bit. Surf. Repair			509-4, 1665 Gal./Mi. Maint. Dept.	
1941	A.F.E. 67	Spot Treat. Bit. Surf. Repair			504, 2351 Gal./Mi. Maint. Dept.	
1942	A.F.E. 4	Spot Treat. Bit. Surf. Repair			RT6, 3946 Gal./Mi. Grav. 150 C.Y./Mi. Maint. Dept.	
1943	A.F.E. 4	Spot Treat. Bit. Surf. Repair			Oil 4573 Gal./Mi. Grav. 223 C.Y./Mi. Maint. Dept.	
1944	A.F.E. 4	Spot Treat. Bit. Surf. Repair			Oil 4563 Gal./Mi. Grav. 106 C.Y./Mi. Maint. Div.	
1946	1207-05 1207-08	Grading Gravel	36'	1 1/2"	(2) Lengthens 0.08 5.99	
1947	A.F.E. 6	Grav. Resurfacing			3224 C.Y. 5.99	
1949	1207-09	Stab. Gravel Base Mixed Bit.	32' 26'	9" 1"	5.99	
1950	A.F.E. 4	Bit. Fog Seal	24'		RC-1 & 2, 9544 Gal. Agg. 308 C.Y. 5.99	
1992	1207-10	Plant Mix Bit.	24'	1 1/2"	5.99	

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED			INCORPORATED			RURAL		URBAN	
			RDWY. MI.	BR. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	
1921	1945	5.91	5.91	0.00	0.00	0.00	5.91	0.00	0.00	0.00		
1946		5.99	5.99	0.00	0.00	0.00	5.99	0.00	0.00	0.00		

REMARKS: Layout is to scale as of 1921.

(1) This work not done under this project number but lies within the limits of this project.


(2) New length is from P.I. at W. Jct. T.H. 40 to P.I. at E. Jct. T.H. 40.

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1207
TRUNK HIGHWAY 29
COUNTY Chippewa
DISTRICT BA

LIMITS: W. Jct. T.H. 40 - E. Jct. T.H. 40
Ref. Pt. 012+00.299 - 018+00.288

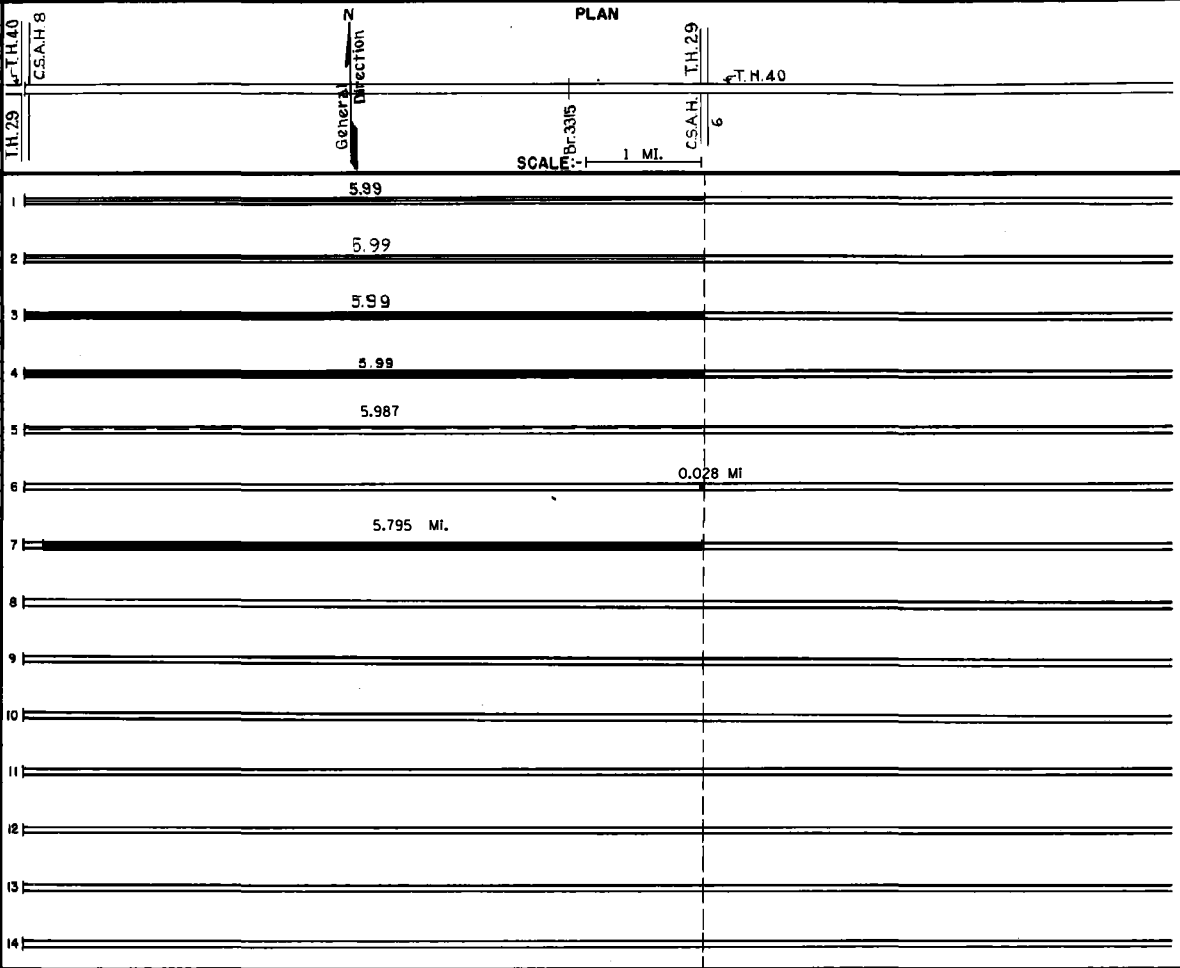

YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
M 1955	A.F.E. 605	Bit. Seal Coat	24'		RC-4, 16779 Gal. Agg. 690 C.Y.	1
M 1967	C	Light Bit. Seal	25'		CRS-1 Bit. 12,604 Gal. FA-1 Agg. 476 C.Y.	2
C 1971	1207-11	Pl. Mix Bit. Gravel Shoulder	24'	1 1/2"		3
C 1985	1207-17	Bit. Surfacing Agg. Shoulders	24'	3" Var.	Sp. 2331	4
M 1990	M4418	Bit. Sealing				5
S 2001	1210-09	Bit. Overlay	24'	1 1/2"		6
M 2002	1207-18	Bit. Overlay & Shoulders	24'	1.5" 6' 1.5"	Spec. 2350 Spec. 2350	7
						8
						9
						10
						11
						12
						13
						14

YEARS FROM TO		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1
