


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3009
TRUNK HIGHWAY 65
COUNTY Isanti
DISTRICT 38

LIMITS: Jct. T.H. 107 - No. Co. Line



YEAR BUILT	PROJECT N ^o	DESCRIPTION			CODE N ^o
		TYPE	WIDTH	THICKNESS	
C	1941 3009-05	Br. 8532			C12/2X40.
C	1942 3009-04 3009-02	Grading	36'		50 Mi. of divided Highway. Each roadway 30' wide.
C	1942 A.F.E. 7	Seeding			Seed supplied by R.S.D. (S.P. 3009-06/07) Maint. Dept.
C	1943 3004-20	Stab. Gravel Base Mixed Bit.	58' 48'	2" 1"	24' Surf. on each roadway.
C	1943 3009-09	Stab. Gravel Base Mixed Bit.	32' 26'	12" 1"	
M	1945 3009-11	Bit. Surf. Repair (Spots)			
M	1947 A.F.E. 4	Spot Treat. Bit. Surf. Repair			SC-3, 13502 Gal. Agg. 895 C.Y.
M	1948 A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		SC-3, 8119 Gal. Agg. 658 Tons
M	1949 A.F.E. 4	Spot Treat. Bit. Surf. Repair	26'		MC-3, 4027 Gal. Agg. 336 Tons
M	1950 A.F.E. 4	Spot Treat. Bit. Surf. Repair	24'		SC-4, 7760 Gal. Agg. 686 Tons
C	1952 3009-13	Bit. Stab. Grav. Base Plant Mix Bit.	3060' 2448'	0-13" 1 1/2"	Added thickness
M	1957 A.F.E. 605	Bit. Seal Coat			RC-5, 10742 Gal. Agg. 356 C.Y.
M	1958 A.F.E. 606	Shoulder Re-gravel			1908 Tons
C	1965 3009-15/16	Grading Plant Mix Bit. Bit. Shoulders	2448'	3 1/2"	Rt. & Lt. of rdwy. in Var. leveling course

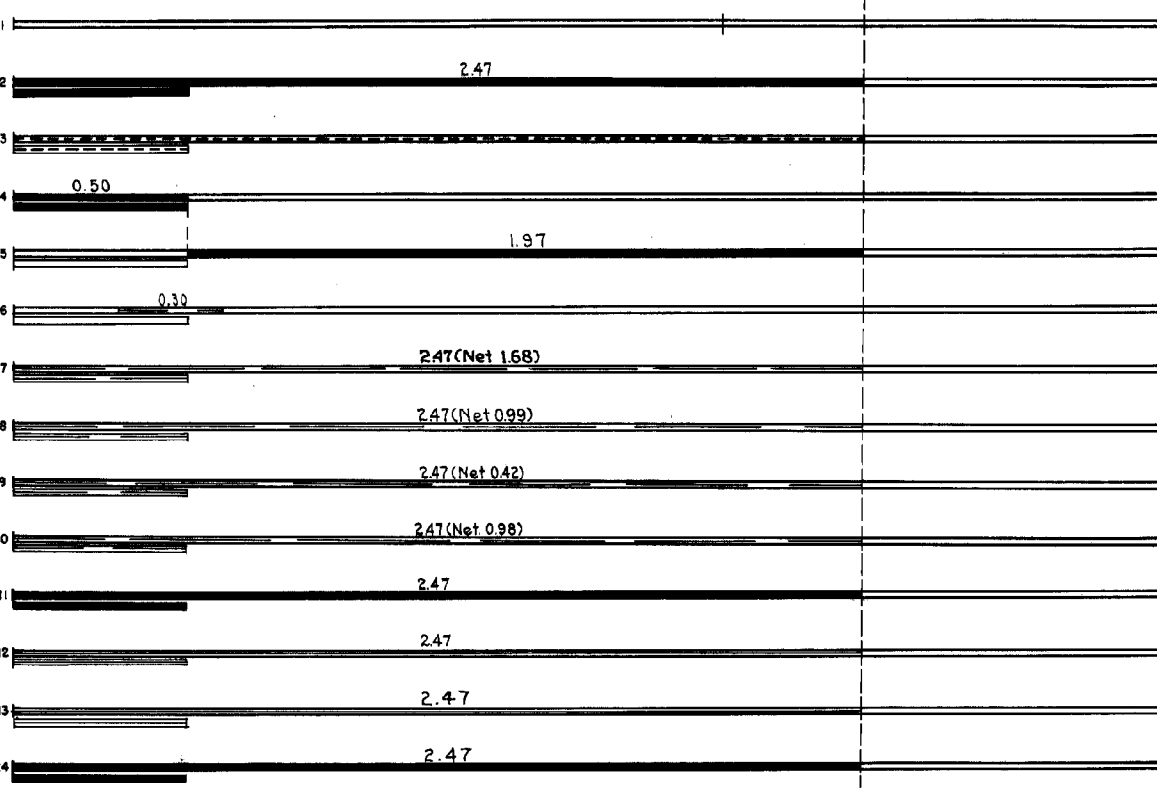

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1942		2.47	2.47	0.00	0.00	0.00	2.47	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1942

