


PREPARED BY
TRANSPORTATION PLANNING AND PROGRAMMING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4680A
TRUNK HIGHWAY 90
COUNTY Martin
DISTRICT 7B

LIMITS: W. Martin Co. - Jct. T.H. 263



YEAR BUILT	PROJECT NO	DESCRIPTION	WIDTH	THICKNESS	REMARKS
C 1973	IG 090-2 (37) 081	Grading & Bridges 91216, 91217, & 46801			C108D & C 108T 279' PPG
C 1973	IG 090-2 (44) 086	Grading & Bridges 46803, 46804, & 46805, & 46806			(2) 143' PPG (2) 143' PPG
C 1974	IG 090-2 (48) 082	Grading & Bridges 46807, 46808, & 46832			(2) 144' PPG 279' PPG
C 1974	IG 090-2 (48) 082	Br. 46830 Br. 46811, 46812			183' DPG (2) 203 PPG
C 1974	IG 090-2 (51) 081	Gravel Base P.C. Concrete Pl. Mix Bit Shoulders	30' 6" 28'24"	6" 9"	10' out & 3' in
C 1975	IG 090-2 (51) 081	Gravel Base P.C. Concrete Pl. Mix Bit Shoulders	28'24"	9"	Gravel Base 30' width & 6" thickness * 10' out & 3' in
M 1979	SF	Wedge Paving Wedge Shoulders			
C 1980	4680-24 (51) 081	Highway Safety Restraint			At C.S.A.H. 23
M 1980	SF	Wedge Paving	24'	1/2"	Pl. Mixed AC A 1/2 Aggregate
M 1981	SF	Bit. Shoulder Overlay	10'	1 1/2"	EB Roadway
C 1982	4680-46814 (51) 081	App. Panel O.L. Br. 46814, 46823 Deck O.L. Bit. Shldr. Replace - O.L.			
M 1982	SF	Seal Coat			CRS-2 & FA-1 Wide Shoulders
C 1984	4680-78 (R 090-21101)	Br. 46807 & 46808 Deck Repair & Overlay	40'-6"	3"	Contract No. 19087
M 1985	SF	Wedge Paving	6'	1"	Sp. 2331 (A) 120 Tons Sp. 2331 570 Tons with Only Wide Shldr.

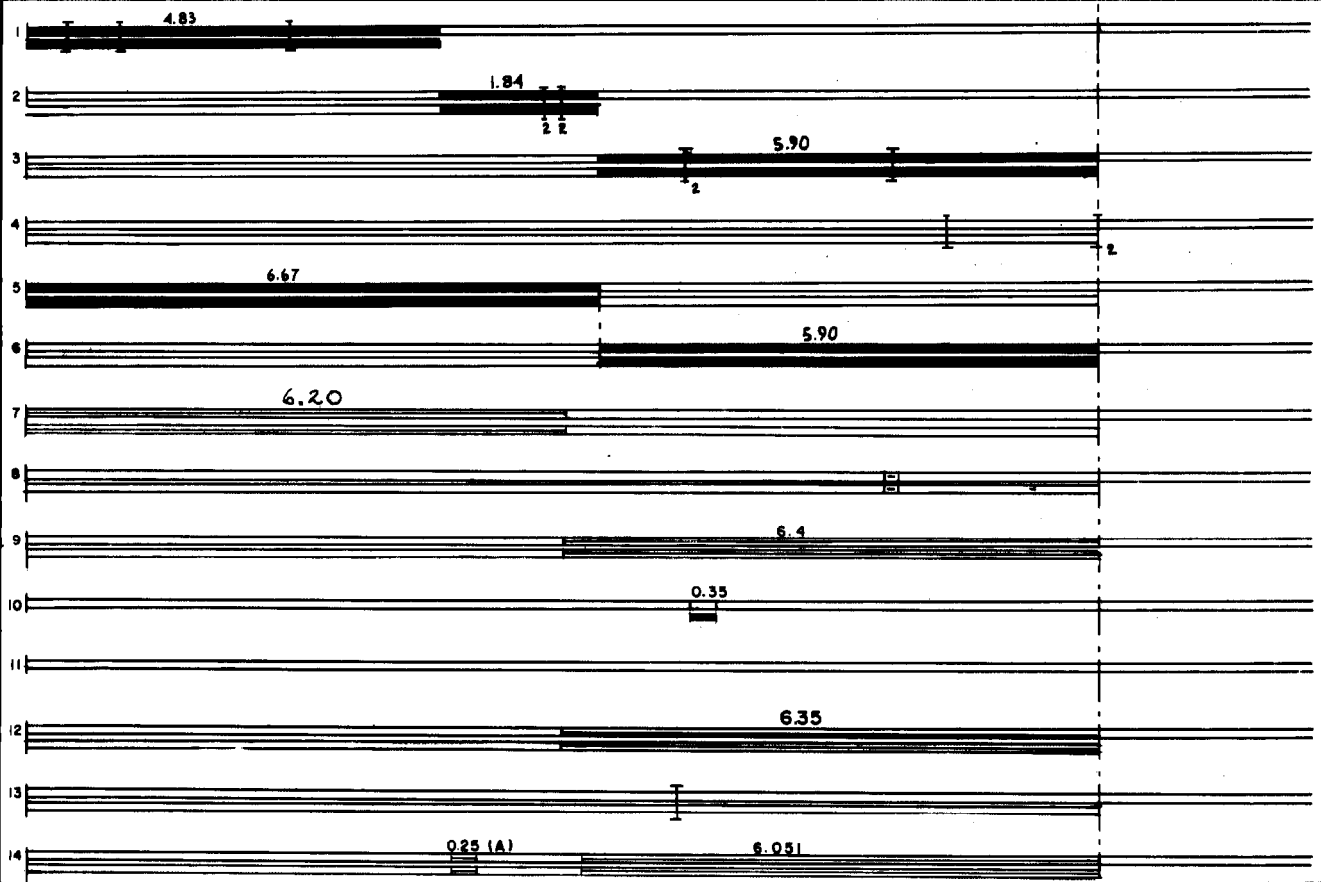

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
		12.57	12.16	0.14	0.27			12.16	0.14	0.27

REMARKS: Layout is to scale as of 1974

