


R.L.-7 REV. 2-40
 PREPARED BY
 HIGHWAY PLANNING SURVEY
 IN COOPERATION WITH
 U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
 DEPARTMENT OF HIGHWAYS
 ROAD LIFE STUDIES
 CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 4710
 TRUNK HIGHWAY 22
 COUNTY Mooker
 DISTRICT 3B-8A

LIMITS: N. Jct. T.H. 12 N. of Litchfield - N. Co. Line in Eden Valley

Ref. Pt. 145+00.044 - 157+00.139

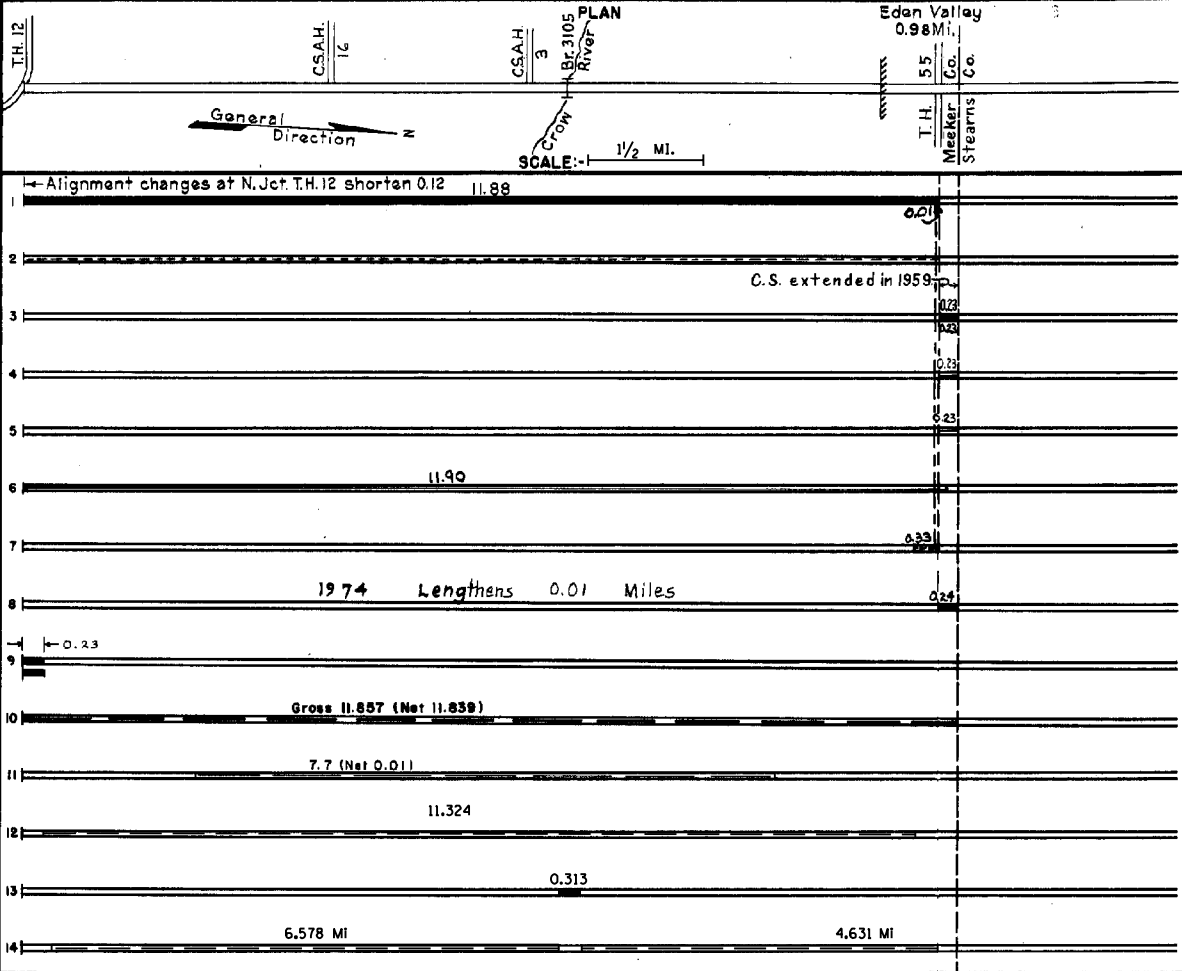

YEAR BUILT	PROJECT N#	DESCRIPTION			CODE N#
		TYPE	WIDTH	THICKNESS	
C 1953	4710-05	Concrete	22'	9 7/8"	1
C 1954	A.F.E. 907	Seeding			2
		Mixed Bit.	63'		3
				No Record of Const. Added in 1959.	
M 1960		Bit. Resurfacing		114 Tons Bit. Mat'l.	4
M 1965	C	Light Bit. Seal	24'	RS-1C, 1196 Gal. Agg. 46 C.Y.	5
M 1974	SF	Joint & Crack Seal		90,148 Lin. Ft.	6
C 1975	RF 060-1 (32)	Widening		0.01 Mi. Reconstruction	7
C 1975	4710-10 RS 4169 (1)	Resurfacing Cure & Gutter	62'		8
C 1979	SF	Bit. Surfacing CHANNELIZATION	2 1/2'	2 1/4" Old Conc. Removed	9
M 1984	SF	Joint Repair Crack Repair		85,910 Lin. Ft. 3,992 Lin. Ft. Seal 35,981 Lbs.	10
M 1984	SF	Conc. Spot Repair	11' 12"	45 1/2 Cu. Yds.	11
M 1991	M4496	Edge Drains			12
C 1993	4710-18	Grading Bit. Surfacing	6 1/2' 28' 1 1/2'	Spec. 2331 Spec. 2341	13
M 1999	M99080	Crack Sealing			14

YEARS FROM TO		TOTAL MILES	UNINCORPORATED ROWY. MI. BR. MI.		INCORPORATED ROWY. MI. BR. MI.		RURAL ROWY. MI. BR. MI.		URBAN ROWY. MI. BR. MI.	

REMARKS: See Sheet No. 1

