


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 5109
TRUNK HIGHWAY 267
COUNTY Murray
DISTRICT 88

LIMITS: Jct. S.A.R. 10 in Iona - Jct. T.H. 30

Ref. Pt. 000+00.000 - 005+00.360



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Mixed Bit.	64'		
		Gravel Br. 6955 & 6956	32'		
M 1949	A.F.E. 6	Grav. Resurfacing			2624 Tons
C 1951	A.F.E. 17	Gravel Base (5.27 Mi.) Bit. Surfacing Mixed Bit.	32' (17) 24'	6" 1'	SG143, 64255 Gal. Agg. 3930 Tons
M 1952	A.F.E. 5	Light Bit. Seal	24'		RS 152, 9288 Gal. Agg. 365 T.Y.
M 1954	A.F.E. 604	Bit. Surf. Repair	24'		SC-3, 4250 Gal. Agg. 325 Tons
M 1955	A.F.E. 604	Bit. Surf. Repair	24'		SC-3, 6055 Gal. Agg. 280 Tons
M 1956	A.F.E. 604	Spot Treat Bit. Surf. Repair	24'		SC-3, 13942 Gal. Agg. 1025 Tons
M 1958	A.F.E. 604	Spot Treat Bit. Surf. Repair	24'		SC-3, 10015 Gal. Agg. 799 Tons
M 1960		Spot Treat Bit. Surf. Repair	24'		SC-3, 9948 Gal. Agg. 652 Tons
M 1962		Bit. Surf. Repair			Rd. Mix 59 Tons Tack SC-3, 740 Gal.
C 1973	5109-01	Bit. Surface	24'	3"	
M 1985	4158	Bit. Overlay	24'	1 1/2"	Spec. 2331
M 1994	94154	Bit. Overlay	24'	1 1/2"	Spec. 2341

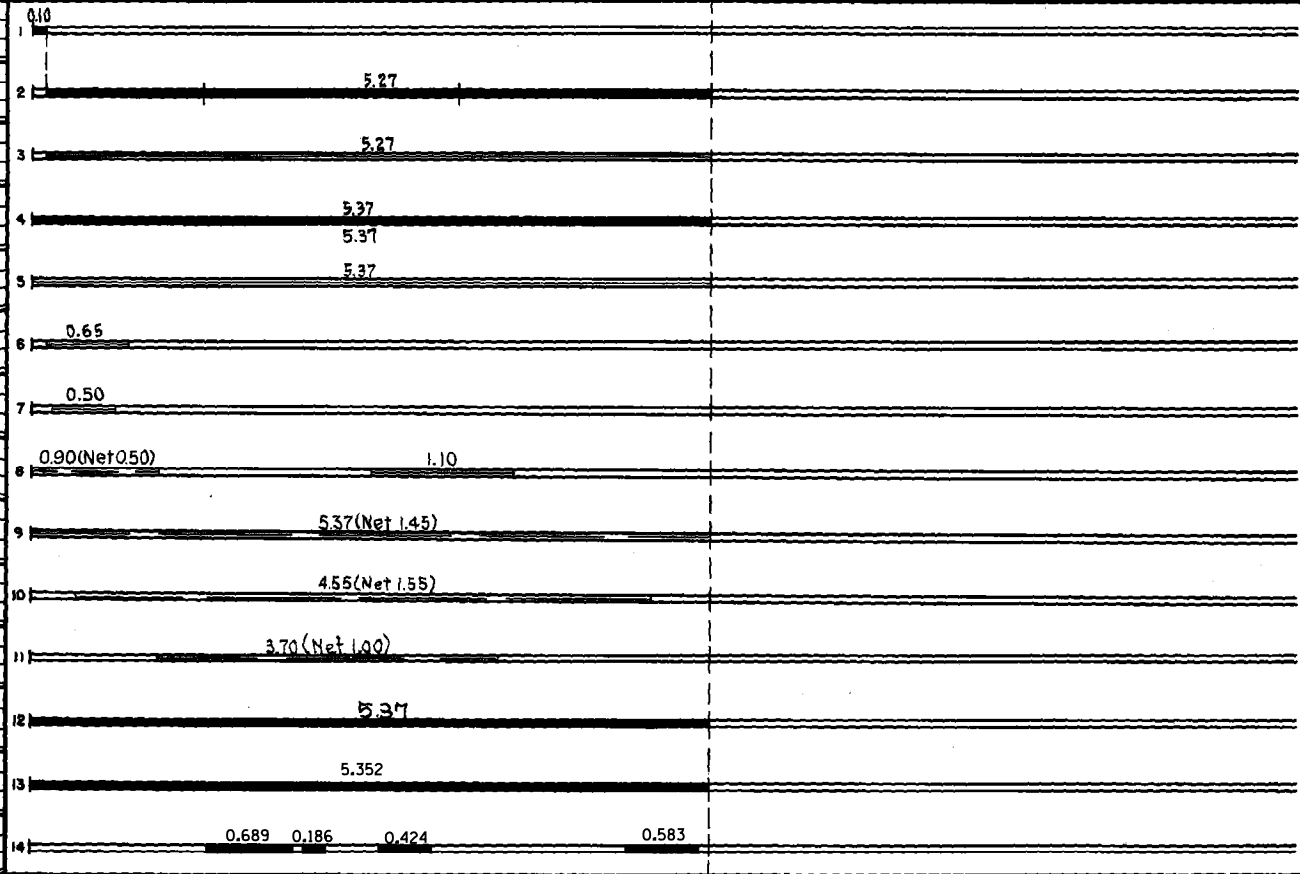

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1950		5.37	4.99	0.00	0.38	0.00	5.37	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1950
(1) Bit. Resurfacing center 24' of 64' Rwy. from Mi. Pt. 0.00-0.10.

