


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6404  
TRUNK HIGHWAY 19  
COUNTY Redwood  
DISTRICT 8B

LIMITS: Jct. T.H. 71 in Redwood Falls - N. End of Bridge (Minn. River).



YEAR BUILT	PROJECT N <sup>o</sup>	DESCRIPTION			CODE N <sup>o</sup>
		TYPE	WIDTH	THICKNESS	
		Gravel	20'	2"	No Record of Constr.
		Br. M-119	20'		360 H.T. & Approach
1921	19-14-9	Concrete	36'		No Record of Constr.
1928	19-14-24-4B	Grading	32'		
		Br. 4479, 4668, 4667, & 4666	27'		40 C.D.G. 178 C.D.G. - D.H. 120 H.T. & 290 H.T. & T.
1929	19-14-24-4B	Gravel	24'	3 1/2"	1600 C.Y./Mile.
1930	19-14-24-4A	Grading	40'		
		Gravel	32'	1"	600 C.Y./Mile.
1931	19-14-24-4A&B	Concrete	20'	9'-9"	
C	A.F.E. 52	Improved Should.			*1 1/2" Pl. Mix. Bit on 2 1/2" Stab. Grav. Maint. Dept.
M	A.F.E. 26	Storm Sewer			In Redwood Falls
	A.F.E. 27	Replace Cattle Pass			Under Br. 4479
C	6404-02	Base Widening (I)			2-24" Plant Mix Bit.
1953	6404-02	Plant Mix Bit.	44'	3 1/2"	Service Drives Const.
	6404-04	Street Lighting			From M.I. Pt. 058-089
C	1960	Replace portals & raise lower cross-frames on Brs. 4666 & 4667			By Br. Crew No. 2
C	1965	Gravel Shoulders	20'	3" 4"	MC-800 Tack 1867 Gal. Bit. Mix 7304 Tons
1966	C	Plant Mix Bit. Seal	21'		CRS-1,540 Gal.
C	1970	6404-11	Pl. Mix Bit.	44'	3"
C	1970	6404-10	Pl. Mix Bit. Shlds. Pl. Mix Bit. Base & Overlay	24'	3"
M	1971	6404-12	Pl. Mix Bit. Resurf.	20'	3/4"

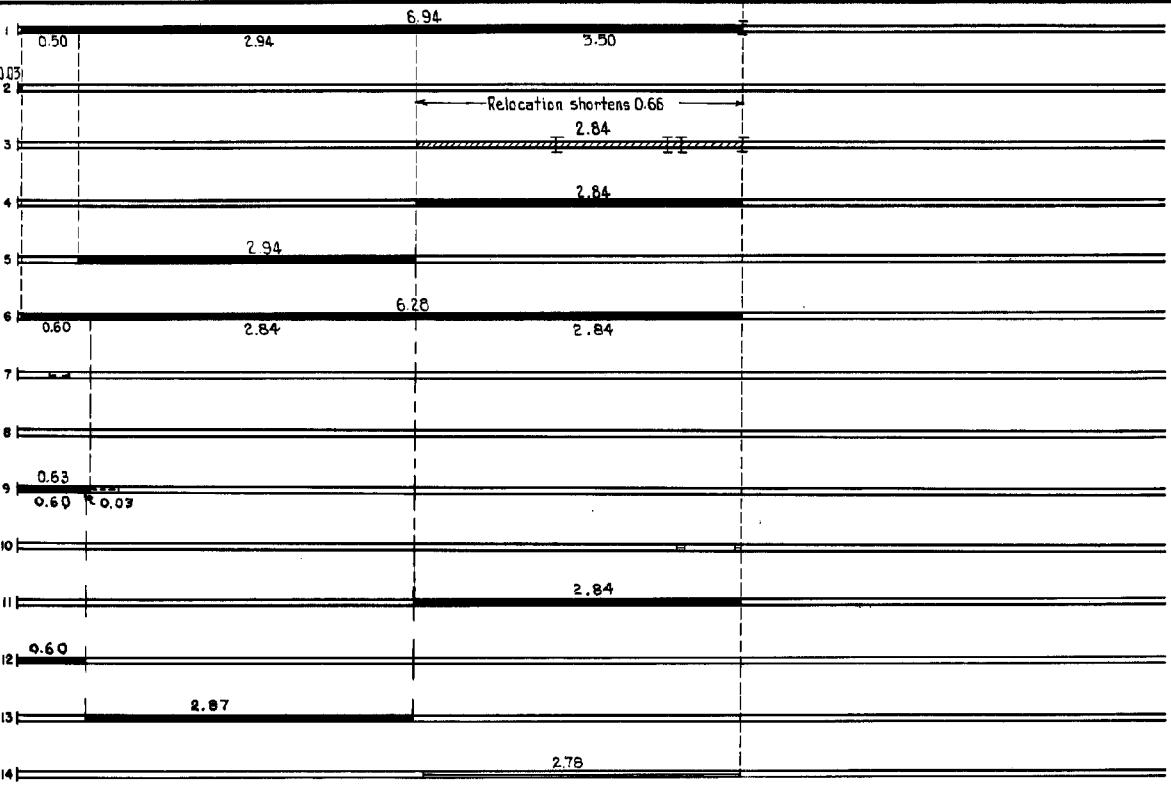

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1927	1927	6.3	5.81	0.07	1.09	0.00	5.81	0.07	1.09	0.00
1928	1957	6.3	5.10	0.12	1.05	0.00	5.10	0.12	1.05	0.00
1958	1964	6.3	5.19	0.12	1.00	0.00	5.19	0.12	1.00	0.00
1965		6.3	4.59	0.12	1.60	0.00	4.59	0.12	1.60	0.00

REMARKS: Layout is to scale as of 1928.  
0120-26 Concr. Imp. widened to 44 with 8" Concr. Base or 12" Bit. Stab. Base

10-74



