


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD


CONTROL SECTION 6408
TRUNK HIGHWAY 68
COUNTY Redwood
DISTRICT 8B

LIMITS: N. Jct. T.H. 71 - Jct. T.H. 67 in Morgan

Ref. Pt. 076+00.820 - 086+00.924



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICKNESS	
		Gravel	26'		No Record of Const. Added in 1949
1948	64-516-01	Grading	26'		Added in 1949
		Gravel	26'		No Record of Const. Added in 1949
M	1949 A.F.E. 6	Grav. Resurfacing (Spots)	24'		1408 Tons
C	1951 A.F.E. 4	Bit. Surfacing Mixed Bit.	24'	1"	MC21963, 2755 Gal. Agg. 123 CY.
M	1951 A.F.E. 6	Grav. Resurfacing	24'		6510 Tons
C	1953 6408-01	Sand-Grav. Subbase	24'	6-15"	
		Gravel Base	24'	3"	
		Plant Mix Bit.	24'	1 1/2"	
C	1954 A.F.E. 907	Seeding			
M	1958 A.F.E. 605	Bit. Seal Coat	26'		RC-5, 1202 Gal. Agg. 41 C.Y.
M	1962	Light Bit. Seal	25'		RC-2, 23104 Gal. Agg. 760 C.Y.
C	1972 6408-06	Plant Mix Bit Surf. Gravel Shoulders	24'	1 1/2"	2' Right & Left
M	1984 SF	Chia Seal Coat	30'		CRS-2 @ Quarzite
M	1985 SF	Spot Overlay			
M	1986 4206	Bit. Overlay	24'	1 1/2"	

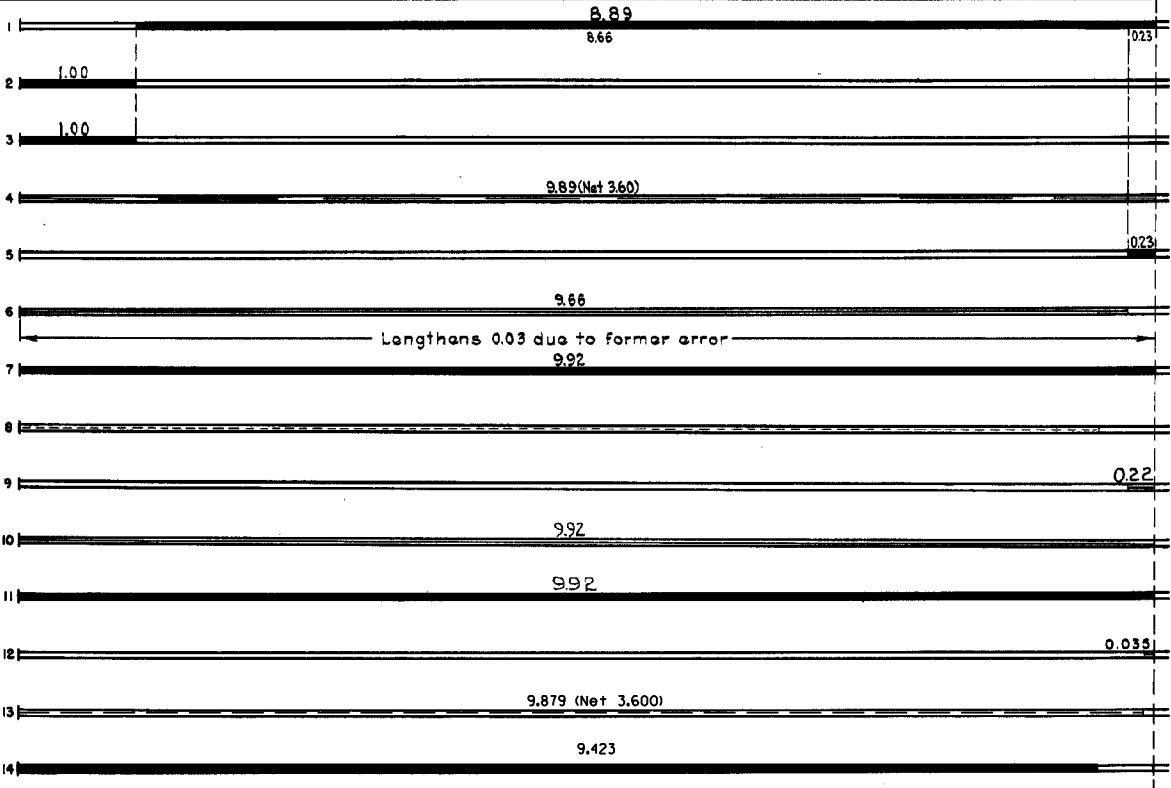

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	1952	9.89	9.40	0.00	0.49	0.00	9.89	0.00	0.00	0.00
1953		9.92	9.43	0.00	0.49	0.00	9.92	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1949

