FORM R.L.-7 REV. 3-58

SHEET 1 OF 1

PREPARED BY
TRAFFIC AND PLANNING DIVISION
IN COOPERATION WITH
U.S. DEPARTMENT OF COMMERCE
BUREAU OF PUBLIC ROADS

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 0283
INTERSTATE TRUNK HIGHWAY 35
COUNTY Anoka
DISTRICT Metro

LIMITS: N. Jct. T.H. 35E & 35W To Washington Co. Line

Ref. Pt. 127+00.420 - 129+00.955

PLAN



YEAR BUILT	PROJECT NO	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C 1969	0283-03	Grading Br. 02806	Var.		Divided Highway 232.8' B.S. - U.P
C 1969	0283-07	Base Concrete Pavement Pl. Mix. Bit. Shldrs.	2@36	5 1/4" 8"	 10' in. & out.
C 1982	0283-02806	Br. Deck Repair & Overlay			
C 1984	0283-17	Conc. Median Rehabilitation	20'	4"	
C 1987	0283-18	Bit. Overlay	Var.	4"	Spec. 2361
C 1991	0283-19	Crack Repair			
C 1997	0283-20	Milling and Surfacing	Var	1-½" 2-½"	61WEA75100 41BIB50070
D 2001	8825-102	Rout & Seal			Spec. 3725
R 2009	0283-26	Milling Bit. Overlay Conc. Rehab.	var. var.	4" 4"	 Spec. 2360

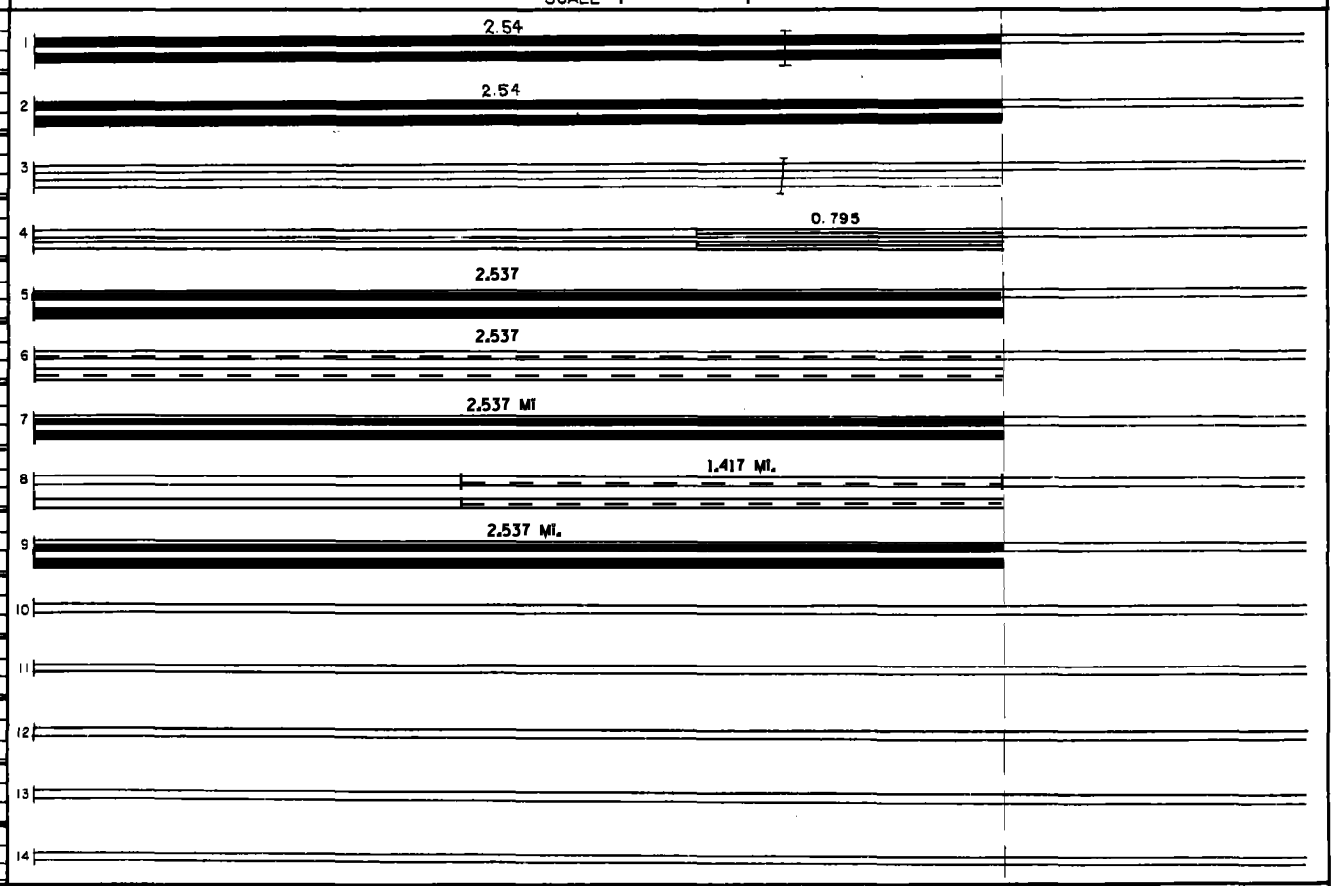

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1969		2.54	2.54	0.00	0.00	0.00	2.54	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1969
