Mn/DOT 29450 (4-78)
FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U.S. DEPARTMENT OF TRANSPORTATION-FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2280
TRUNK HIGHWAY 90
COUNTY FARIBAULT
DISTRICT 7A

LIMITS: Jct. TH 254 — E. Co. Line

Ref. Pt. 128+00.565 - 142+00.792

YEAR BUILT	PROJECT NO	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C 1975	2280-14	GRADING			
		BR 22814			327' PPG U.P.
	I090-2(53)138	BR 22819			349' PPG U.P.
C 1975	2280-32	AGG. BASE	2@40'	6"	(1)
		P.C. CONC. SURF	2@24'	9"	
	I090-2(68)137	BI. MIX BIT. SHOULDERS	10', 3'	2", 9"	10' BIT OUT; 3' CONC IN
C 1976	2280-21	GRADING			
		BR 22812, 22813			308', 305' PREC. CONC. B.S.
	I090-2(62)138	BR 91371			22' CONC. BOX CULV.
C 1976	2280-28	GRADING			
		BR 22820			306' PREC. CONC. B.S.
	I090-2(72)132				
C 1976	2280-62	GRADING			
		BR 22815, 22816			2-106' PREC CONC BS
	I090-2(72)132	BR 91541			3-RCPA - 52'
C 1977	2280-31	AGG BASE	2@40'	5"	
		P.C. CONC. SURF.	2@24'	9"	
	I090-2(62)138	BIT. & CONC. SHOULDERS	10', 3'	2", 9"	
C 1978	2280-43, 44	AGG BASE	2@40'	5"	
		P.C. CONC. SURF	2@24'	9"	
	I090-2(74)132	BIT. & CONC. SHOULDERS	10', 3	9", 9"	
M 1980	SF	Bit. Shoulder Wedge	2'	0-3"	166 Pl. Mix Bit. 615 Gal. RC 250 Tack Portion Only
M 1981	SF	Shoulder Wedge Paving	3'	0"-3"	218.35 Ton 200 Gal. RC 250 Pl. Mix
M 1981	SF	Shoulder Wedge Paving	3'	0"-3"	347.45 Ton 470 Gal. RC 250 Pl. Mix
M 1985	2280-94	Approach Surface Deck Repair Conc. Overlay			Br. 22814
M 1985	2280-95	Approach Surface Deck Repair Conc. Overlay			Br. 22811
C 1985	2280-98	Bit. Shoulders Sub-Surf. Drainage	10'	2"	
C 1988	2280-108	Crack Repair			

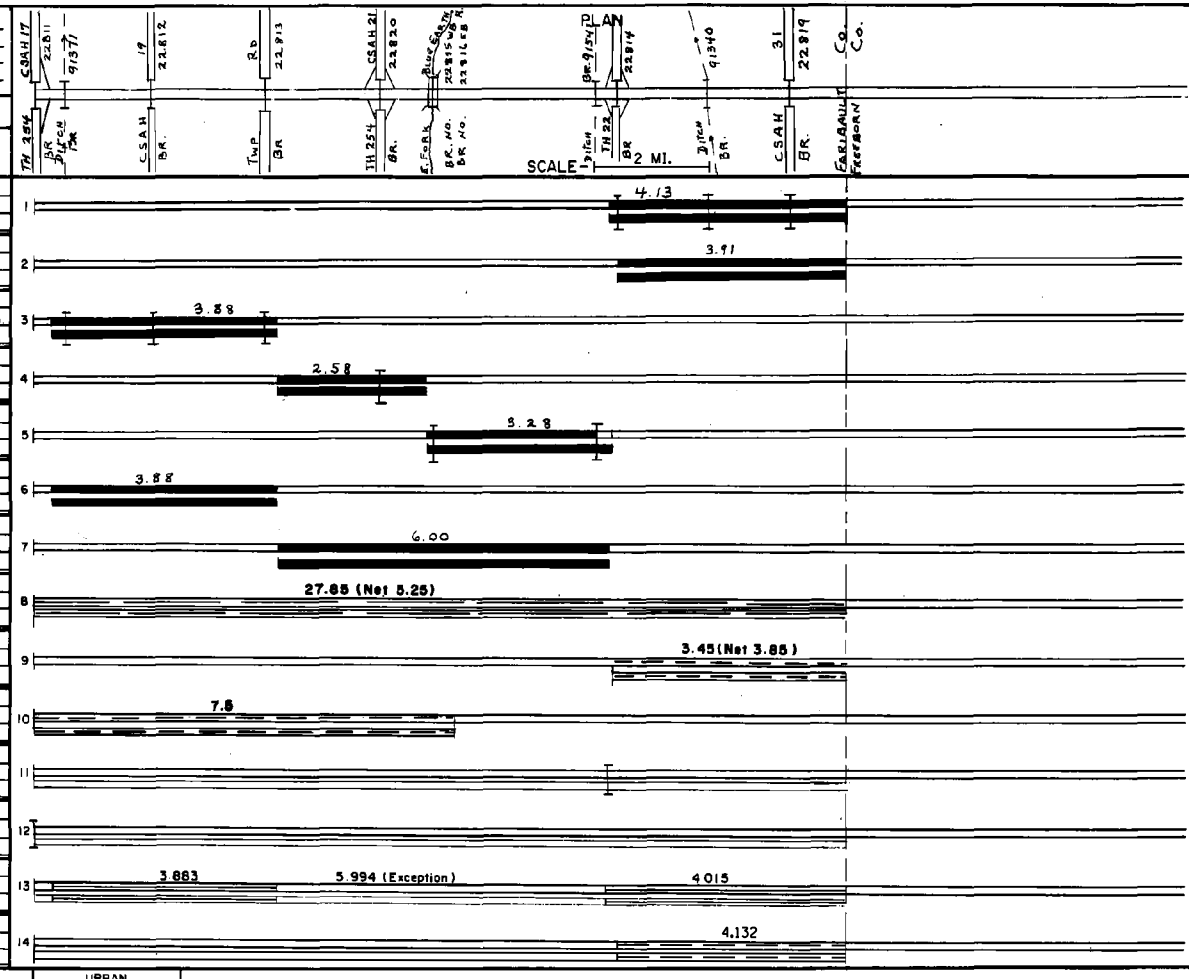

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS: LAYOUT IS TO SCALE OF 1975
(1) 4.01 MI CONST., BUT 0.10 NOT IN USE IN 1975

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 2280B
TRUNK HIGHWAY 90
COUNTY Faribault
DISTRICT 7A

LIMITS: Jct. MNT.H. 254 - Faribault/Freeborn Co. Line

Ref. Pt. 128+00.565 - 142+00.792



YEAR BUILT	PROJECT No	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS
C 1990	2280-109	Conc. Overlay	27'	1½"	
M 1991	2280-106	Joint Repair			
M 1991	SF	Wedge Paving			
C 2000	2280-117	Bituminous Overlay	40'	3"-4"	Spec 2350
M 2003	2280-123	Bituminous Patching			Spec 2360
C 2006	2280-122	Bit. Overlay	24'	Var.	Spec.2360
M 2008	8827-102	Crack Seal			Type 3725
M 2009	2280-126	Concrete Rehab.			
C 2014	8827-112	Br. Approach Panels Br.'s 22803, 22804, 22806 Br.'s 22815, 22816, 22825, 22826			
C 2014	2280-132	Unbond. Conc. Overlay	Var.	Var.	
M 2019	8827-304	Sealcoat & Fogseal			WB EB

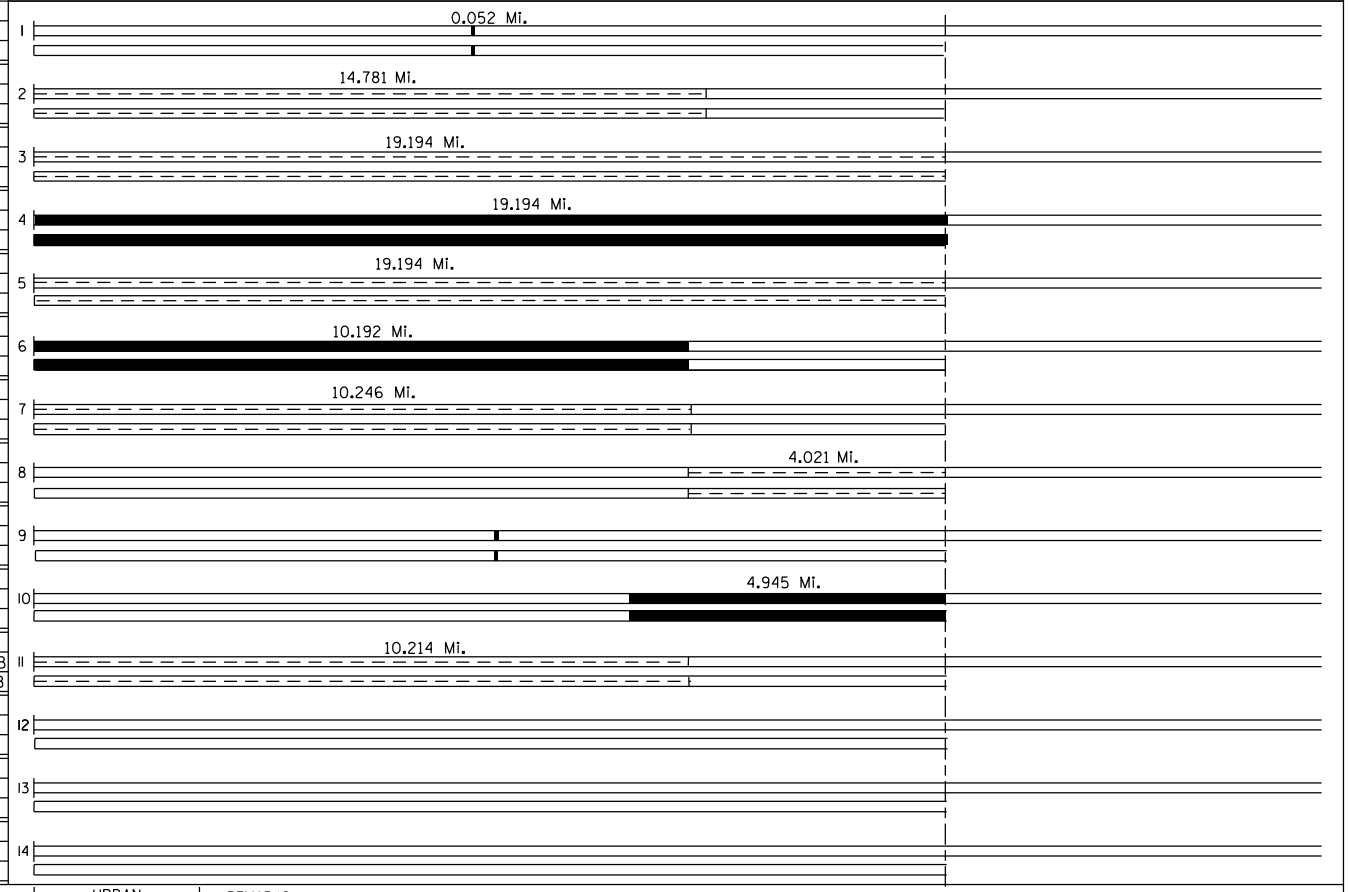

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
